

TECHNICAL INSPECTIONS, INC.
PO BOX 1307
LOXAHATCHEE, FL 33470
OFFICE (561) 619-5313 FAX (561) 619-5315



INSPECTED BY: MARK Vitale INSPECTION DATE: 11/2/2024

SITE / SUBDIVISION NAME: Fox Trail

CULVERT LOCATION: Fox Trail East just North of the Weir Gate

PIPE SIZE: 54" PIPE LENGTH: 40' TYPE OF CULVERT: RCP CAP CMP

DEPTH FROM SURFACE TO THE TOP OF THE PIPE 4'


DESCRIBE ACCESS TO THE PIPE _____

CHANNELING REQUIRED: YES _____ NO ON WHICH SIDE? _____

PIPE CONDITION: CLEAN _____ 0-3" _____ 0-6" _____ 0-12" _____ 0-18" _____ 3" _____ 3-6" _____ 6"
6-12" _____ 12" _____ 12-18" _____ 12-24" _____ 18" _____ 18-24" _____ 24"+ _____

GENERAL CONDITION OF THE PIPE: Fair but Crushed on the North end and lifted up

CULVERT PROFILE

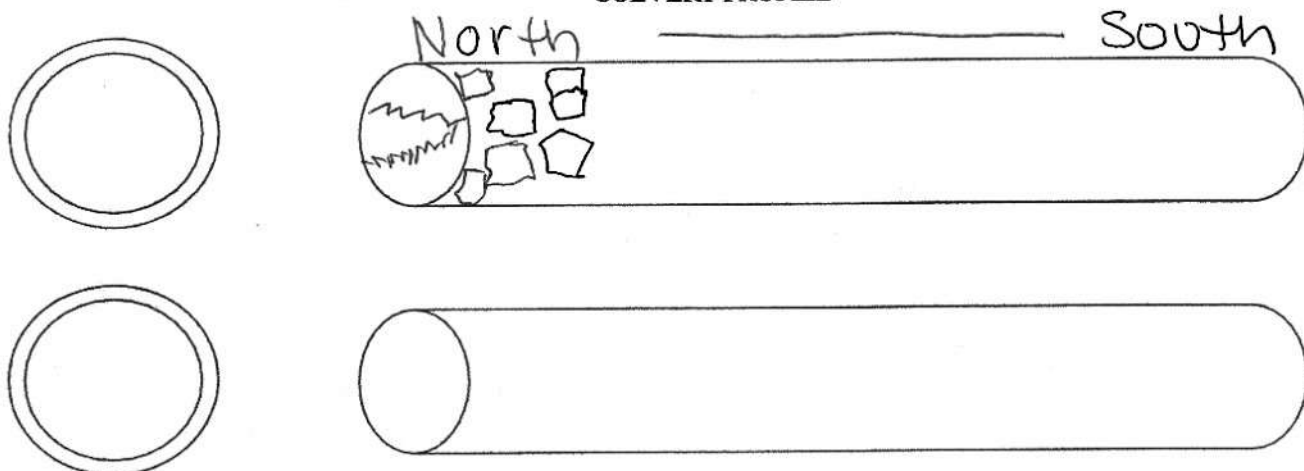

NOTES: Will need to remove large rocks from north of pipe to re-gain flow and straightened where crushed
